

Resiliency Plan Year 1 Checkpoint: August 2026

Resiliency Plan year 1 checkpoint, September 17, 2026. Progress, spend and issues for the nine approved measures at August 31, 2026. Presented by the Resiliency Program Manager.

The plan

Approved by the PUCT on October 23, 2025: nine measures, about \$612 million of capital and \$41 million of O&M over 2026-2028. We filed on April 28, 2025 proposing about \$890 million; the approved plan removed two measures and reduced undergrounding.

Progress: poles, trimming, automation, undergrounding

Units completed against 2026 targets at August 31 (units differ by measure):

Pole replacement and bracing: 3,020 of 4,200 poles

Vegetation cycle acceleration: 188.6 of 330 circuit miles

Feeder automation (IGSD): 115 of 180 devices

Strategic undergrounding: 8 of 21 circuit miles

Progress: substations, cable, transmission, monitoring

Substation flood mitigation: 0 of 2 substations (both in construction)

URD cable replacement: 26 of 38 cable miles

Transmission structure hardening: 84 of 160 structures

Weather stations and damage model: 14 of 14 stations

Substation physical security: 1 of 4 sites


Spend

January-August: \$109.0 million of capital and \$3.37 million of O&M. 2026 capital budget \$196 million; forecast \$180 million, mainly because undergrounding is forecast at \$26 million against \$42 million.

Monthly resiliency capital

Capital recorded against the nine measures by month, January-August 2026.

Monthly resiliency capital • USD

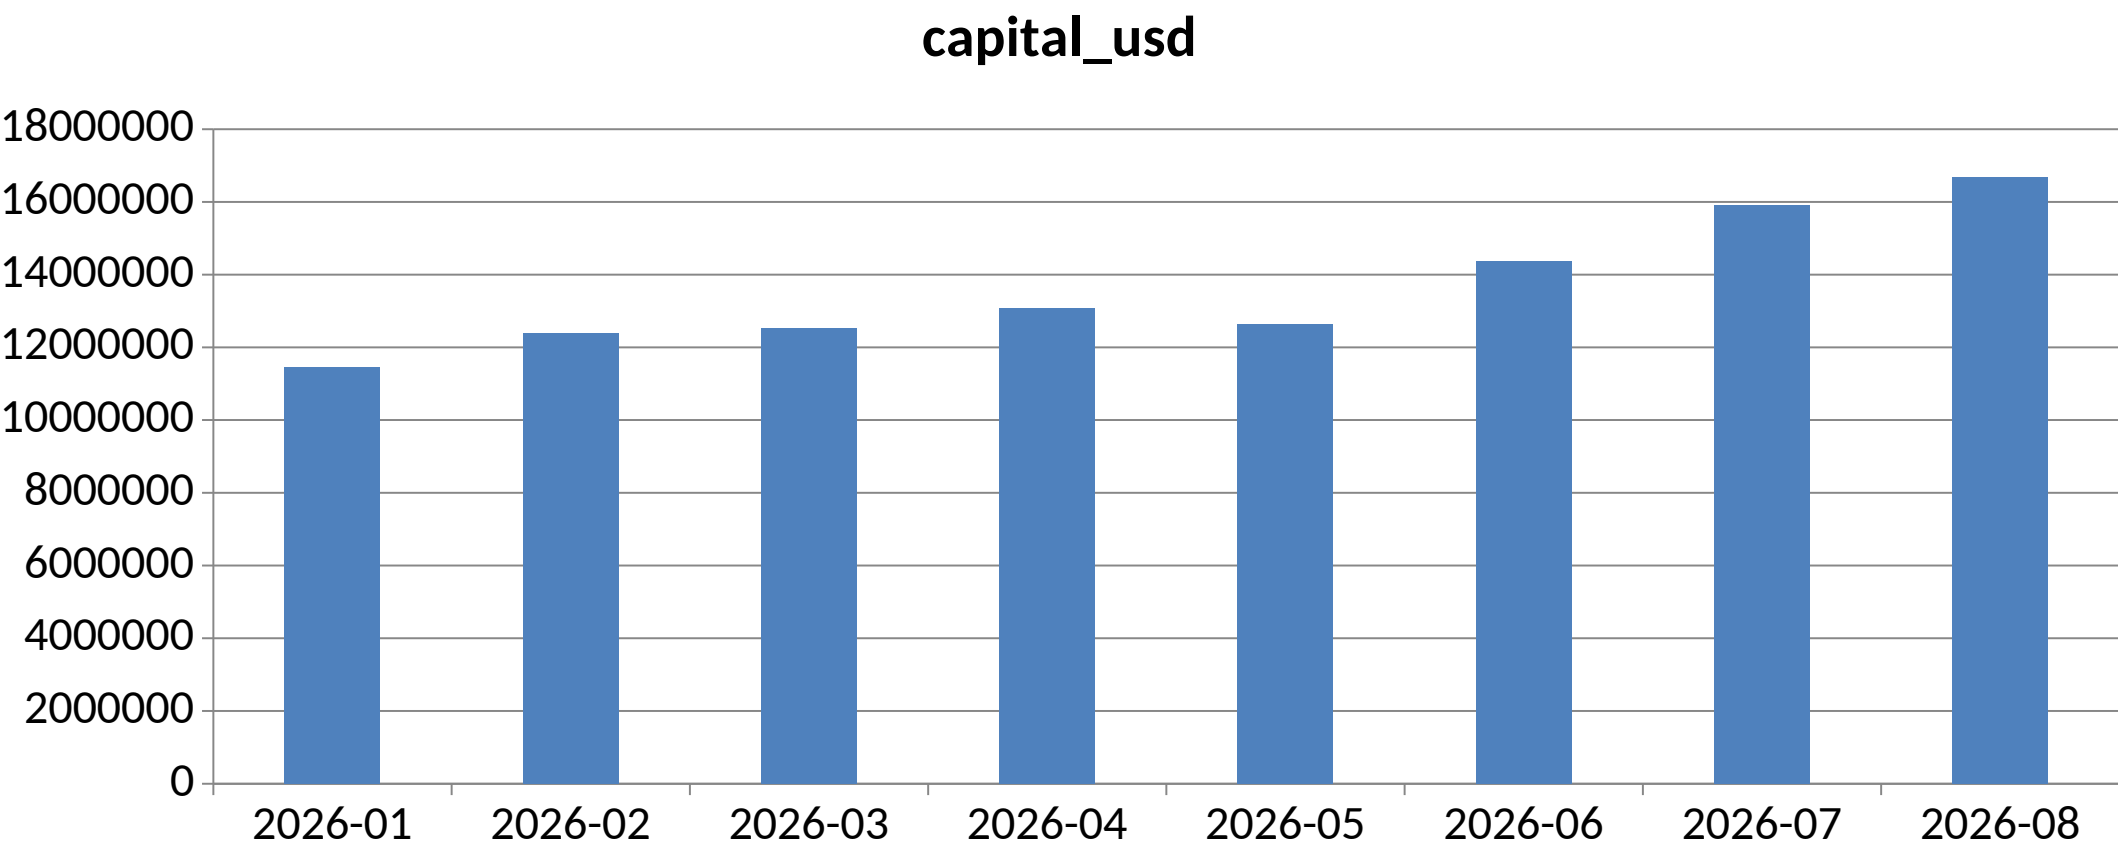

Issue: undergrounding behind plan

Permitting and design took longer than assumed, and two projects were re-scoped to shorter crossings in July. Those two now show forecast in-service dates earlier than baseline because of the smaller scope.

Vegetation acceleration

In-scope Bayou and Prairie feeders move to a three-year cycle. 188.6 of 330 acceleration miles and 1,740.9 of 2,650 cycle miles done or in progress.

Reporting and next plan

First-half progress report filed June 26, 2026; second-half report due December 31. The PUCT must decide a complete plan within 180 days, and an updated plan cannot take effect earlier than three years after the prior approval.
