

Research Leadership Review: Bioanalytical Capacity Options

Research leadership review of bioanalytical capacity options, September 23, 2026. Presented by DMPK & Bioanalytical for the Chief Scientific Officer, research directors and the Finance partner, ahead of the decision on October 2.


The question

How should we add bioanalytical capacity for 2027: buy a second LC-MS/MS triple-quadrupole system, run a second shift, or send more discovery work out? The decision is due on October 2.

Our two LC-MS/MS systems are close to full

June to August: 91% booked and 84% used, against 74% and 67% from March to May. INS-002 lost about 58 hours to an ion-source repair in July. The chart shows used hours across all bookable instruments by month.

Our two LC-MS/MS systems are close to full • hours

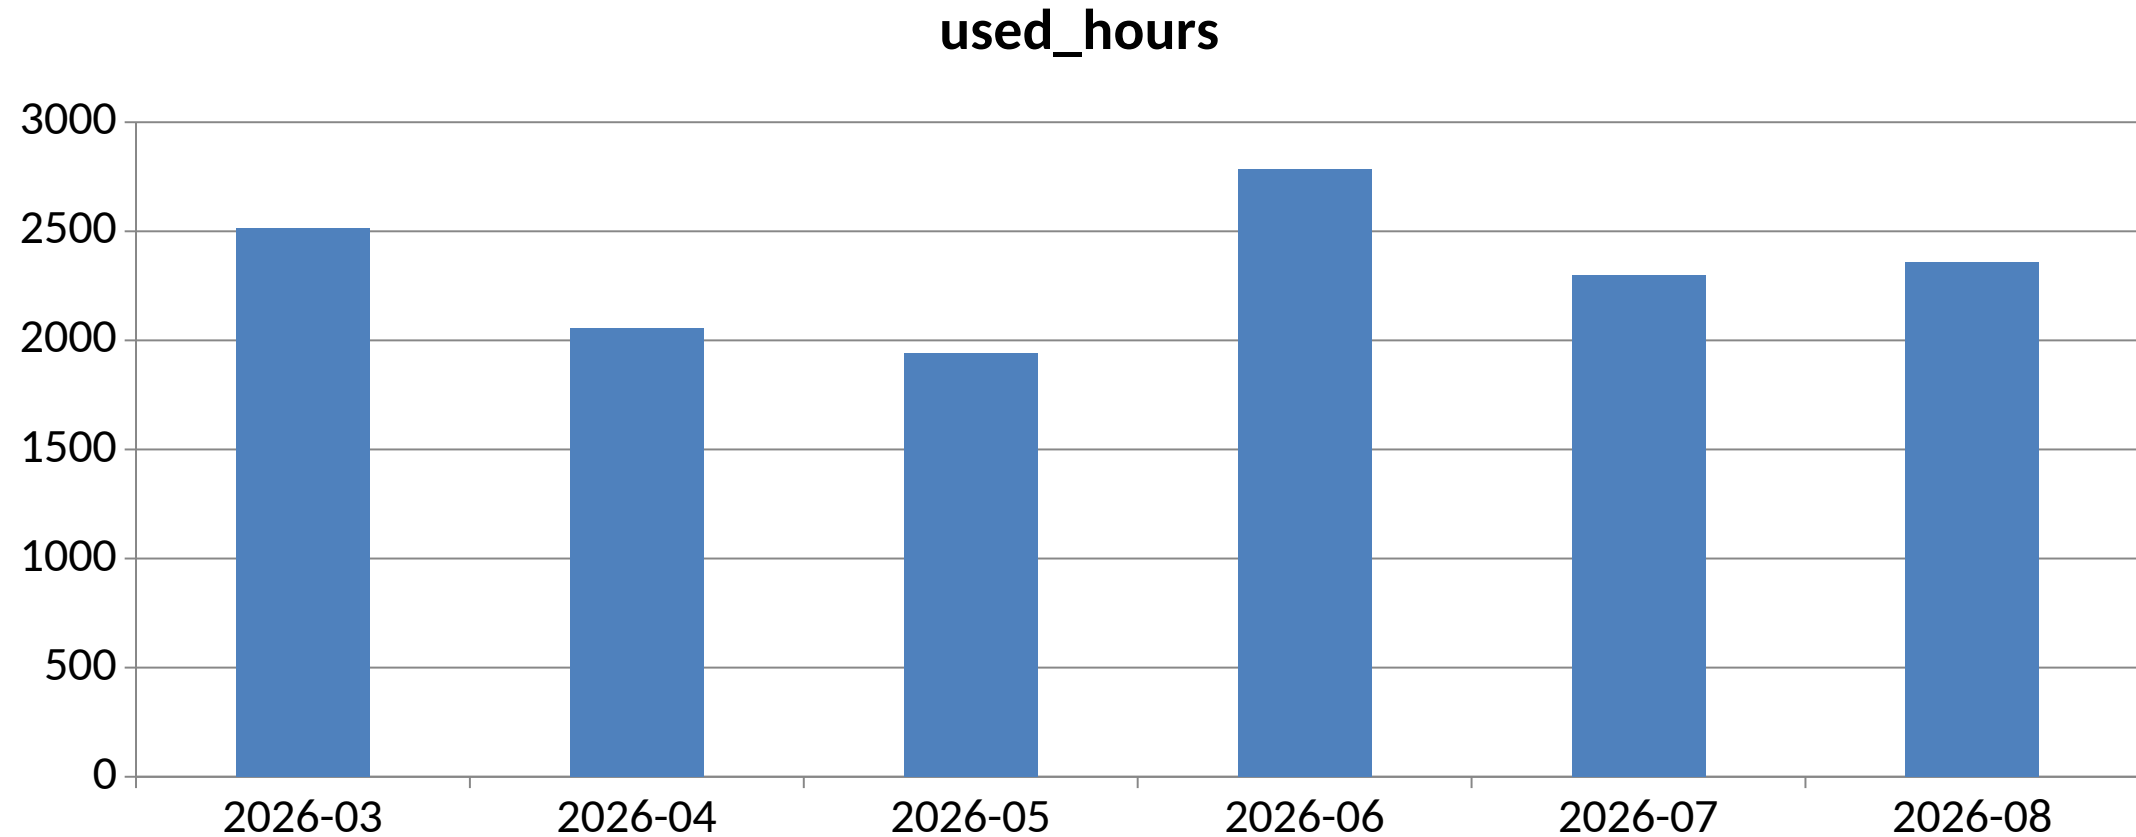

More work is already going out

In-house share of samples fell from 31% in January to May to 15% in June to August. Median shipment to data transfer: 7 days in-house, 22 days external. Alder has taken discovery overflow since June; Fenwick is being qualified as a second lab.

2027 adds demand

DP-07 candidate profiling, LRT-4051 metabolite work and CANOPY-OLE pharmacokinetic sampling. The OLE volume is still an unconfirmed assumption.

Option A – second triple quadrupole

About \$640,000 capital. Six to eight months to routine use, so not before the second quarter of 2027. Restores in-house turnaround and protects against a single outage.

Option B – second shift

One additional scientist on the existing systems. Quicker and cheaper than a new system, but no help when an instrument is down, and it depends on hiring.

Option C – outsource more

About \$30,000 a month at current volume. No capital and flexible, but discovery waits about three weeks for results, and the same labs will carry more clinical and IND work.

Choice left open

The design proposal does not recommend an option. The discussion today should settle which criteria matter most: turnaround for discovery, resilience, cash, and staffing. Combinations are possible, for example B or C as a bridge to A.

Before October 2

Clinical team to confirm CANOPY-OLE sampling volume.

Finance and People to cost a second shift.

QA to give Fenwick qualification timing.

DMPK to refresh the option A quote.
