


R&D Data Hub Phase 2 Proposal Review

Proposal review for R&D Data Hub phase 2, September 17, 2026, for research leadership, IT and the Finance partner. We are asking for approval to plan phase 2, not to build it.

The problem: results reach teams days after the run

January to August 2026: median 4 days from assay run to registry upload, 90th percentile 11 days; DP-09 runs took a median of 7 days. The delay is mostly the manual ELN-to-registry step. The chart shows plates run by month.

The problem: results reach teams days after the run • plates

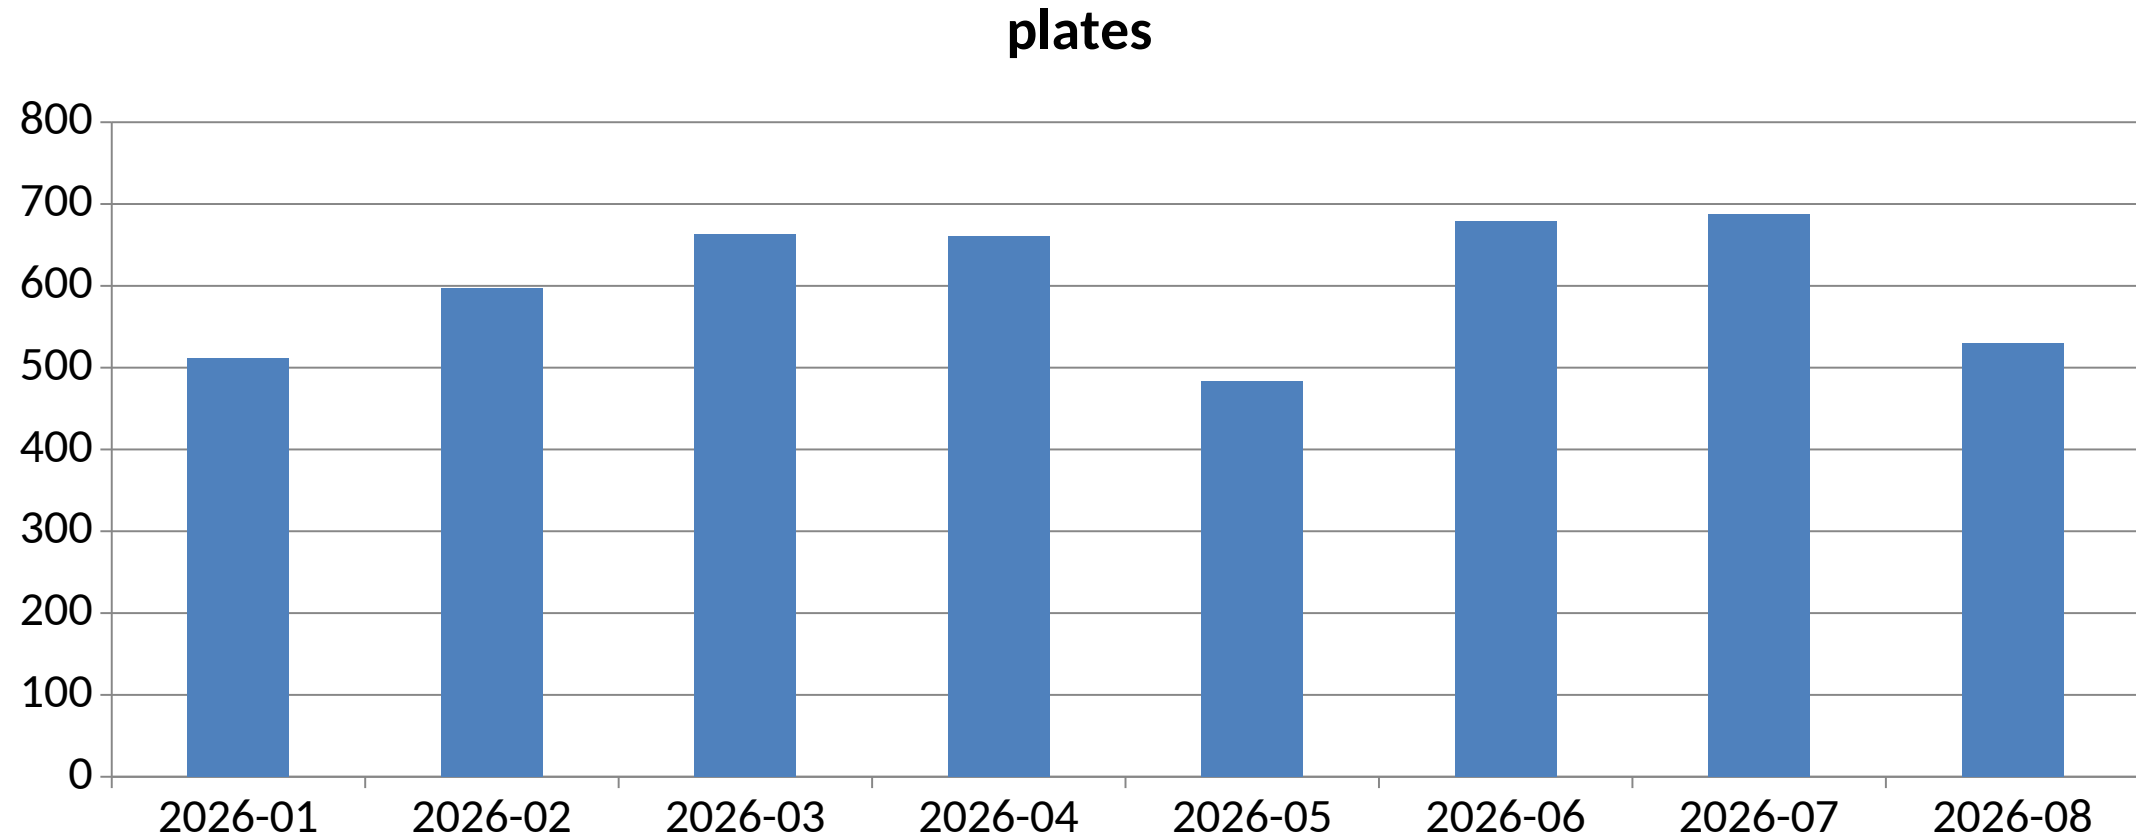

Quality is not the issue

1,305 of 1,450 runs passed acceptance criteria, 103 were repeated and 42 invalidated. Phase 2 is about speed and handling, not about changing review rules.

How data flow today

Instruments and the chromatography data system feed ELN experiments; scientists export and import runs into the assay registry by hand; the registry and compound database load into the Data Hub each night. Phase 1 has run since March 2025. External transfers arrive as files and are not in the Data Hub.

How data flow today • interfaces

Instrument data server and chromatography data system → Electronic lab notebook
results attached to

Electronic lab notebook → Assay & sample registry
run records uploaded to

Assay & sample registry → R&D Data Hub
nightly load into

External data are growing

85% of bioanalytical samples went to external labs from June to August, and central lab transfers for CANOPY-1 moved from every two weeks to weekly in June. Each transfer is checked and read from files, outside the Data Hub.

Proposed scope

Direct ELN-to-registry transfer for the main assay families, replacing manual export and import.

Intake of external bioanalytical results and CRO transfers into a controlled area of the Data Hub, with the existing receipt checks.

Dashboards that show pending uploads and reviews by project.

Out of scope

Replacing the ELN, the registry or the compound database.

Any change to GxP clinical systems hosted by the CRO.

Unblinded clinical data of any kind.

Effort and dependencies

Rough effort: 9 to 12 person-months across Research Informatics, IT and the ELN vendor over two quarters; no cost estimate yet. Depends on ELN vendor interface support, on Bayou Managed IT for infrastructure, and on agreeing transfer formats with Alder and the CRO.

Decision requested

Phase 2 is a proposal and has not been approved or budgeted. We ask for approval to prepare a planning package, with cost, vendor options and a validation approach for the external intake, by October 30, 2026.
