

External Partner Performance Review — Q3 2026 Interim

Interim Q3 2026 review of external partner performance for the outsourcing steering group (Clinical Operations, CMC, QA and Finance), September 22, 2026. Deliverables due January to August, status as of September 18. Purpose: agree follow-up actions before the Q4 oversight reviews.

Scope and data window

493 contracted deliverables due January to August 2026, from the deliverables tracker. Work orders and partner tiers from the register as of September 18: 97 active or pending work orders with \$116.6 million of committed services.

Invoice accuracy is not reported this quarter; the Finance extract was not ready.

Scope and data window • extract summary

Measure: committed_usd

Unit: USD

Total: 128091000.0

Mean: 1164463.6364

Records: 110

Period: 2023-01-01 to 2026-09-18

Scope and data window • extract summary

Measure: pass_through_estimate_usd

Unit: USD

Total: 38660000.0

Mean: 2416250.0


Records: 16

Period: 2023-01-01 to 2026-09-18

Overall timeliness: 87% on time

487 of 493 received; 87% on or before the due date; 14 returned for revision; 6 not received. Monthly on-time share ranged from 76% in January to 91% in May and June. The chart counts on-time deliverables by due month.

Overall timeliness: 87% on time • flag

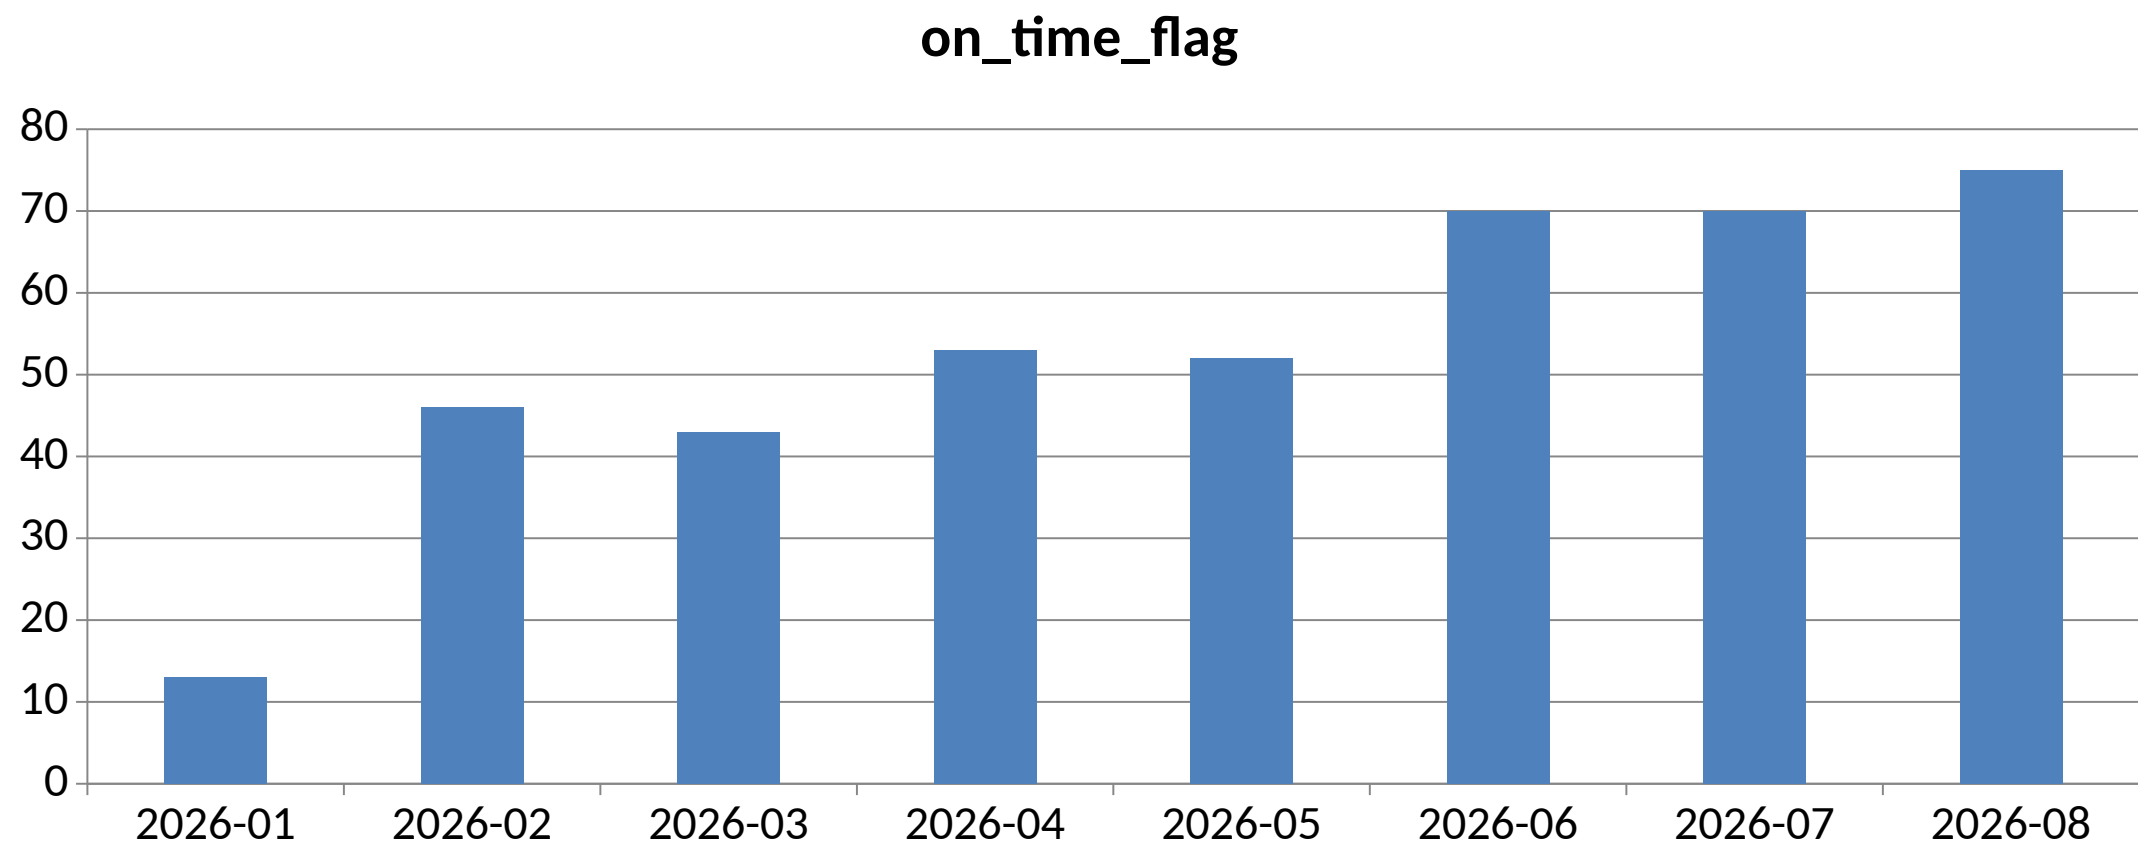

Exception 1 – CDMO executed batch records

Executed batch records were on time for 9 of 16 (56%). Tessaro delivered 4 of 8 on time and Hanlin 0 of 2; Northgate delivered 5 of 6. Batch records gate QA release, so late records delay supply and the LRT-4051 GMP API.

Exception 2 – final study reports

Final study reports were on time for 15 of 24 (62%). Alder Bioanalytical delivered 3 of 8 on time; its overall on-time share across 55 deliverables is 78%, the lowest among high-volume partners. Alder now also takes discovery overflow, so the load is rising.

Backup API supplier

Hanlin Pharmatech delivered 9 of 15 qualification-batch deliverables on time. Its audit response has not yet been accepted and the qualification batch is forecast for February 2027. QA leads the follow-up; this group tracks timeliness only.

Review workload

Median review time after receipt: QA 6 days, Finance 3 days, technical 4 days. QA reviews certificates of analysis, batch records, stability results and final study reports.

Actions and owners

Tessaro: agree batch-record turnaround target at the October business review – CMC & Clinical Supply.

Alder: capacity and report-writing plan for Q4 – DMPK & Bioanalytical with Outsourcing.

Hanlin: timeliness review at the next qualification checkpoint – CMC & Clinical Supply.

Invoice accuracy measure for Q4 reviews – Finance.

Confirm audit dates for 8 partners due by December 31 – QA.

Audits due by year end

8 partners have a routine audit or qualification follow-up due by December 31: Alder Bioanalytical, Aster Archive Services, Northgate Pharma Services, Brookmoor Analytical, Oakmont Statistical Programming, Harborview DSMB Services, Inkwell Medical Writing and Linden Biostatistics.

Data limitations

Timeliness counts a deliverable as on time or late regardless of how late; a batch record one day late counts the same as one a month late. Deliverables due after August are excluded. Quality events are reported by QA separately and are not joined to deliverables in this extract.
